

Sumpter Township Water Department

23480 Sumpter Road Belleville, MI 48111


Phone: (734) 461-6201 Ext. 2242

Fax: (734) 461-6268

Force Main Sewer Tap

SITE LOCATION:				
Address				
Property Tax ID # 81	CANCEL VIOLENCE AND ADDRESS AN			
OWNER INFO:				
Name				
Address				
CityState_		Zip		
Phone (home)(other)				
CONTRACTOR INFO:				
Name				
Address				
City	State	Zip		
Phone (home) Township License #				
**** OFFICE USE ONLY ****				
Planning/Zoning/Ordinance Revi	iew:			
Approved by: Date				
Comments:				
Sewer Department Review:				
Approved by:	Date_			
Comments:				

FORCE MAIN SEWER TAP APPLICATION SUMPTER TOWNSHIP

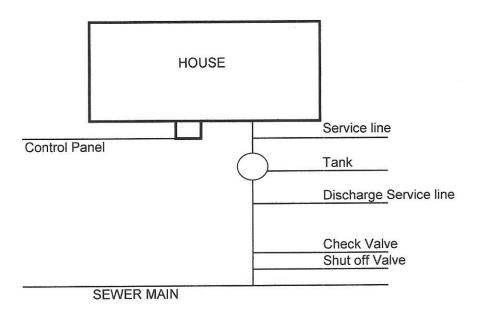

SUMPTER TOWNSHIP PROVIDES

E/ONE SIMPLEX GRINDER PUMP STATION

DH071-93 Tank only, 32' Cable 240V Extreme Core Grinder Pump Sentry Simplex Panel Tank Wrench Asm, LG, for 93" Station Installation of Check Valve and Site Shutoff Valve INSPECTION OF THE ENTIRE PROECES

HOMEOWNER / CONTRACTOR RESPONSIBILITIES

INSTALLATION OF:

- 1. DH071-93 TANK
- 2. Service line from House to the Tank
- 3. Discharge Service line from Tank to Valves
- 4. Decommission the Septic Tank

ELECTRICIAL CONTRACTOR

- 1. Connect power to to control panel
- 2. Connect power to pump and bury wire.

PROCEDURE:

SUBMIT APPLICATION FORM

Include drawing of site and location of the grinder tank and service lines,
Application will be reviewed by Township oficials.

Pursuant to Sumpter Twp Ordinances Sec. 25-77 and Sec. 25-78

WATER SERVICE CONTRACTORS LICENSE REQUIRED

Pursuant to Sumpter Twp Ordinance Sec. 25-137

ELECTRICAL CONTRACTOR REQUIRED FOR THE INSTALLATION OF THE CONTROL BOX

IF APPROVED, ALL FEES MUST BE PAID TO THE TOWNSHIP BEFORE INSTALLATION

Fees		Grinder unit includes:
\$5,250.00 \$3,980.00 \$500 \$43.78	Connection fee to the Twp Sewer E/One Simplex grinder pump and unit x 1.10% Inspection fee	DH071-93 Tank, 32-ft cable 240v Extreme Core Pump Sentry Simplex Electrical Panel Check valve and Shutoff Valve
\$9,773.78	Total Township Cost	

HOMEOWNER / CONTRACTORS RESPOSIBILITIES

CONTACT MISS DIG

HOMEOWNER / CONTRACTOR REQUIRED TO SCHEDULE INSPECTION 1 DAY (24 HR) BEFORE INSTALLATION OF SERVICE LINES AND DH071-93 TANK.

ACCEPTABLE MATERIAL FOR SERVICE LINES (not provided)

Plastic 1 1/4 service line IPS, rated 160 psi.
Trace wire (10 gauge solid / stranded) taped from the service line to the lid of the can 42-in minimum bury depth.

DH071-93 TANK INSTALLATION REQUIREMENTS

A conctere base must be installed aroung the bottom of the of the tank. Sumpter Twp has a template for this process and it must be returned after use.

A minimum of 3 rebar handles need to be installed into the concrete base for lifting tank into place.

Tank must be installed level/plumb.

Tank must be buried to the "ground burial depth" marked on the tank.

SEPTIC TANK WILL BE DECOMMISSIONED BY CONTRACTOR

The septic tank must be pumped out and solids removed, then crushed and filled with dirt.
