ID	Task Name	Duration	Start	Finish
1	**DEEPHAVEN-2023 STREET & IMPROVEMENTS**	**57 days**	**Thu 5/18/23**	**Fri 8/4/23**
2	**STREET BASE BID**	**57 days**	**Thu 5/18/23**	**Fri 8/4/23**
3	TRAFFIC CONTROL	1 day	Thu 5/18/23	Thu 5/18/23
4	INLET PROTECTION	1 day	Thu 5/18/23	Thu 5/18/23
5	SAWING CONCRETE & BITUMINOUS	1 day	Thu 5/18/23	Thu 5/18/23
6	CLEARING AND GRUBBING	2 days	Fri 5/19/23	Mon 5/22/23
7	SALVAGE MAILBOXES & PLACE TEMP MAILBOXS	3 days	Mon 6/19/23	Wed 6/21/23
8	SALVAGE BRICKS AND FENCE	1 day	Wed 6/21/23	Wed 6/21/23
9	LOWER IRON	1 day	Wed 6/21/23	Wed 6/21/23
10	RECLAIMING	1 day	Thu 6/22/23	Thu 6/22/23
11	REMOVALS	3 days	Fri 6/23/23	Tue 6/27/23
12	STRIP RECLAIM AND STOCKPILE	1 day	Fri 6/23/23	Fri 6/23/23
13	PIPE	10 days	Mon 6/26/23	Fri 7/7/23
14	EXCAVATION COMMON & AGGREGATE BASE	3 days	Mon 7/10/23	Wed 7/12/23
15	CONCRETE WORK & CURING TIME	5 days	Thu 7/13/23	Wed 7/19/23
16	TOLERANCING FOR BITUMINOUS	2 days	Thu 7/20/23	Fri 7/21/23
17	PAVE BITUMINOUS BASE	1 day	Mon 7/24/23	Mon 7/24/23
18	RESTORATION	4 days	Tue 7/25/23	Fri 7/28/23
19	RAISE IRON	1 day	Fri 7/28/23	Fri 7/28/23
20	INSTALL MAILBOXS	3 days	Mon 7/31/23	Wed 8/2/23
21	PAVE BITUMINOUS WEAR	1 day	Thu 8/3/23	Thu 8/3/23
22	STRIPING	1 day	Fri 8/4/23	Fri 8/4/23
23	**GAURDRAIL IMPROVEMENTS**	**15 days**	**Tue 7/11/23**	**Mon 7/31/23**
24	TRAFFIC CONTROL	1 day	Tue 7/11/23	Tue 7/11/23
25	SAWCUT	1 day	Wed 7/12/23	Wed 7/12/23
26	REMOVALS	1 day	Thu 7/13/23	Thu 7/13/23
27	EXCAVATION/AGG BASE	1 day	Fri 7/14/23	Fri 7/14/23
28	CONCRETE	5 days	Mon 7/17/23	Fri 7/21/23
29	PATCH BIT	1 day	Mon 7/24/23	Mon 7/24/23
30	BACKFILL	1 day	Tue 7/25/23	Tue 7/25/23
31	REMOVE AND REPLACE GAURDRAIL	2 days	Wed 7/26/23	Thu 7/27/23
32	RESTORATION	2 days	Fri 7/28/23	Mon 7/31/23

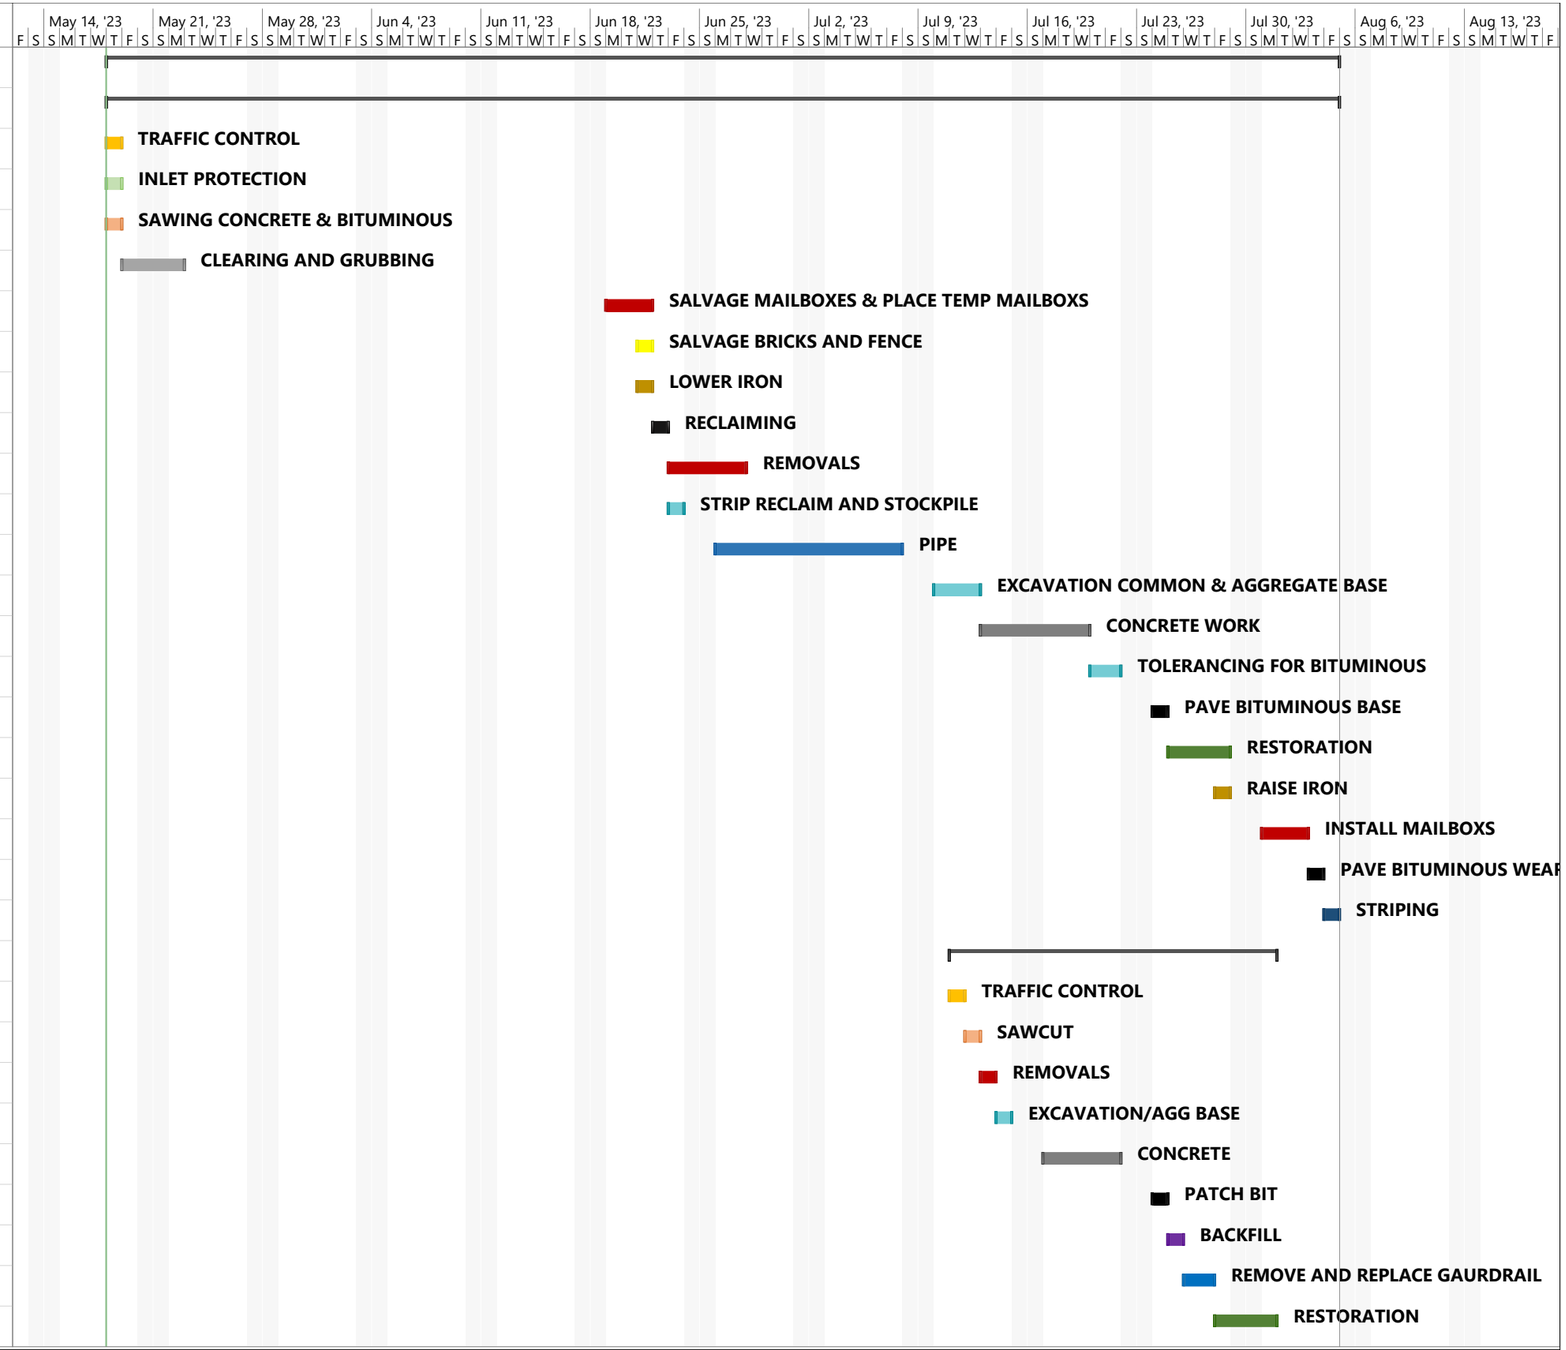

Project: DEEPHAVEN-2023 STR
Date: Thu 5/18/23

Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		
